




**Brickell Place
Structural Milestone Report
List of Remaining Items to be Addressed
As of January 19th, 2026**

- 1. Four Tower Columns (One at a Time)**
 - Shoring Installation
 - Removal of Damaged Sections
 - Placement of New Concrete
 - Removal of Shoring
- 2. Pool Deck Repairs**
 - Three Garage Level Columns
 - Final Deck Repairs
- 3. Section of Deck (South Side of Garage – See Attached Plan, SD-6)**
 - Nine (9) Slab Sections
 - May Involve Joists and Small Beam Sections
- 4. Section of Deck (North Side of Garage – 4 to 5 Bays in Each Direction)**
 - Fresh Survey by ACG – Within a Week
 - Also Mostly Slab Sections
 - At Least Two (2) Joist/Beam Repairs

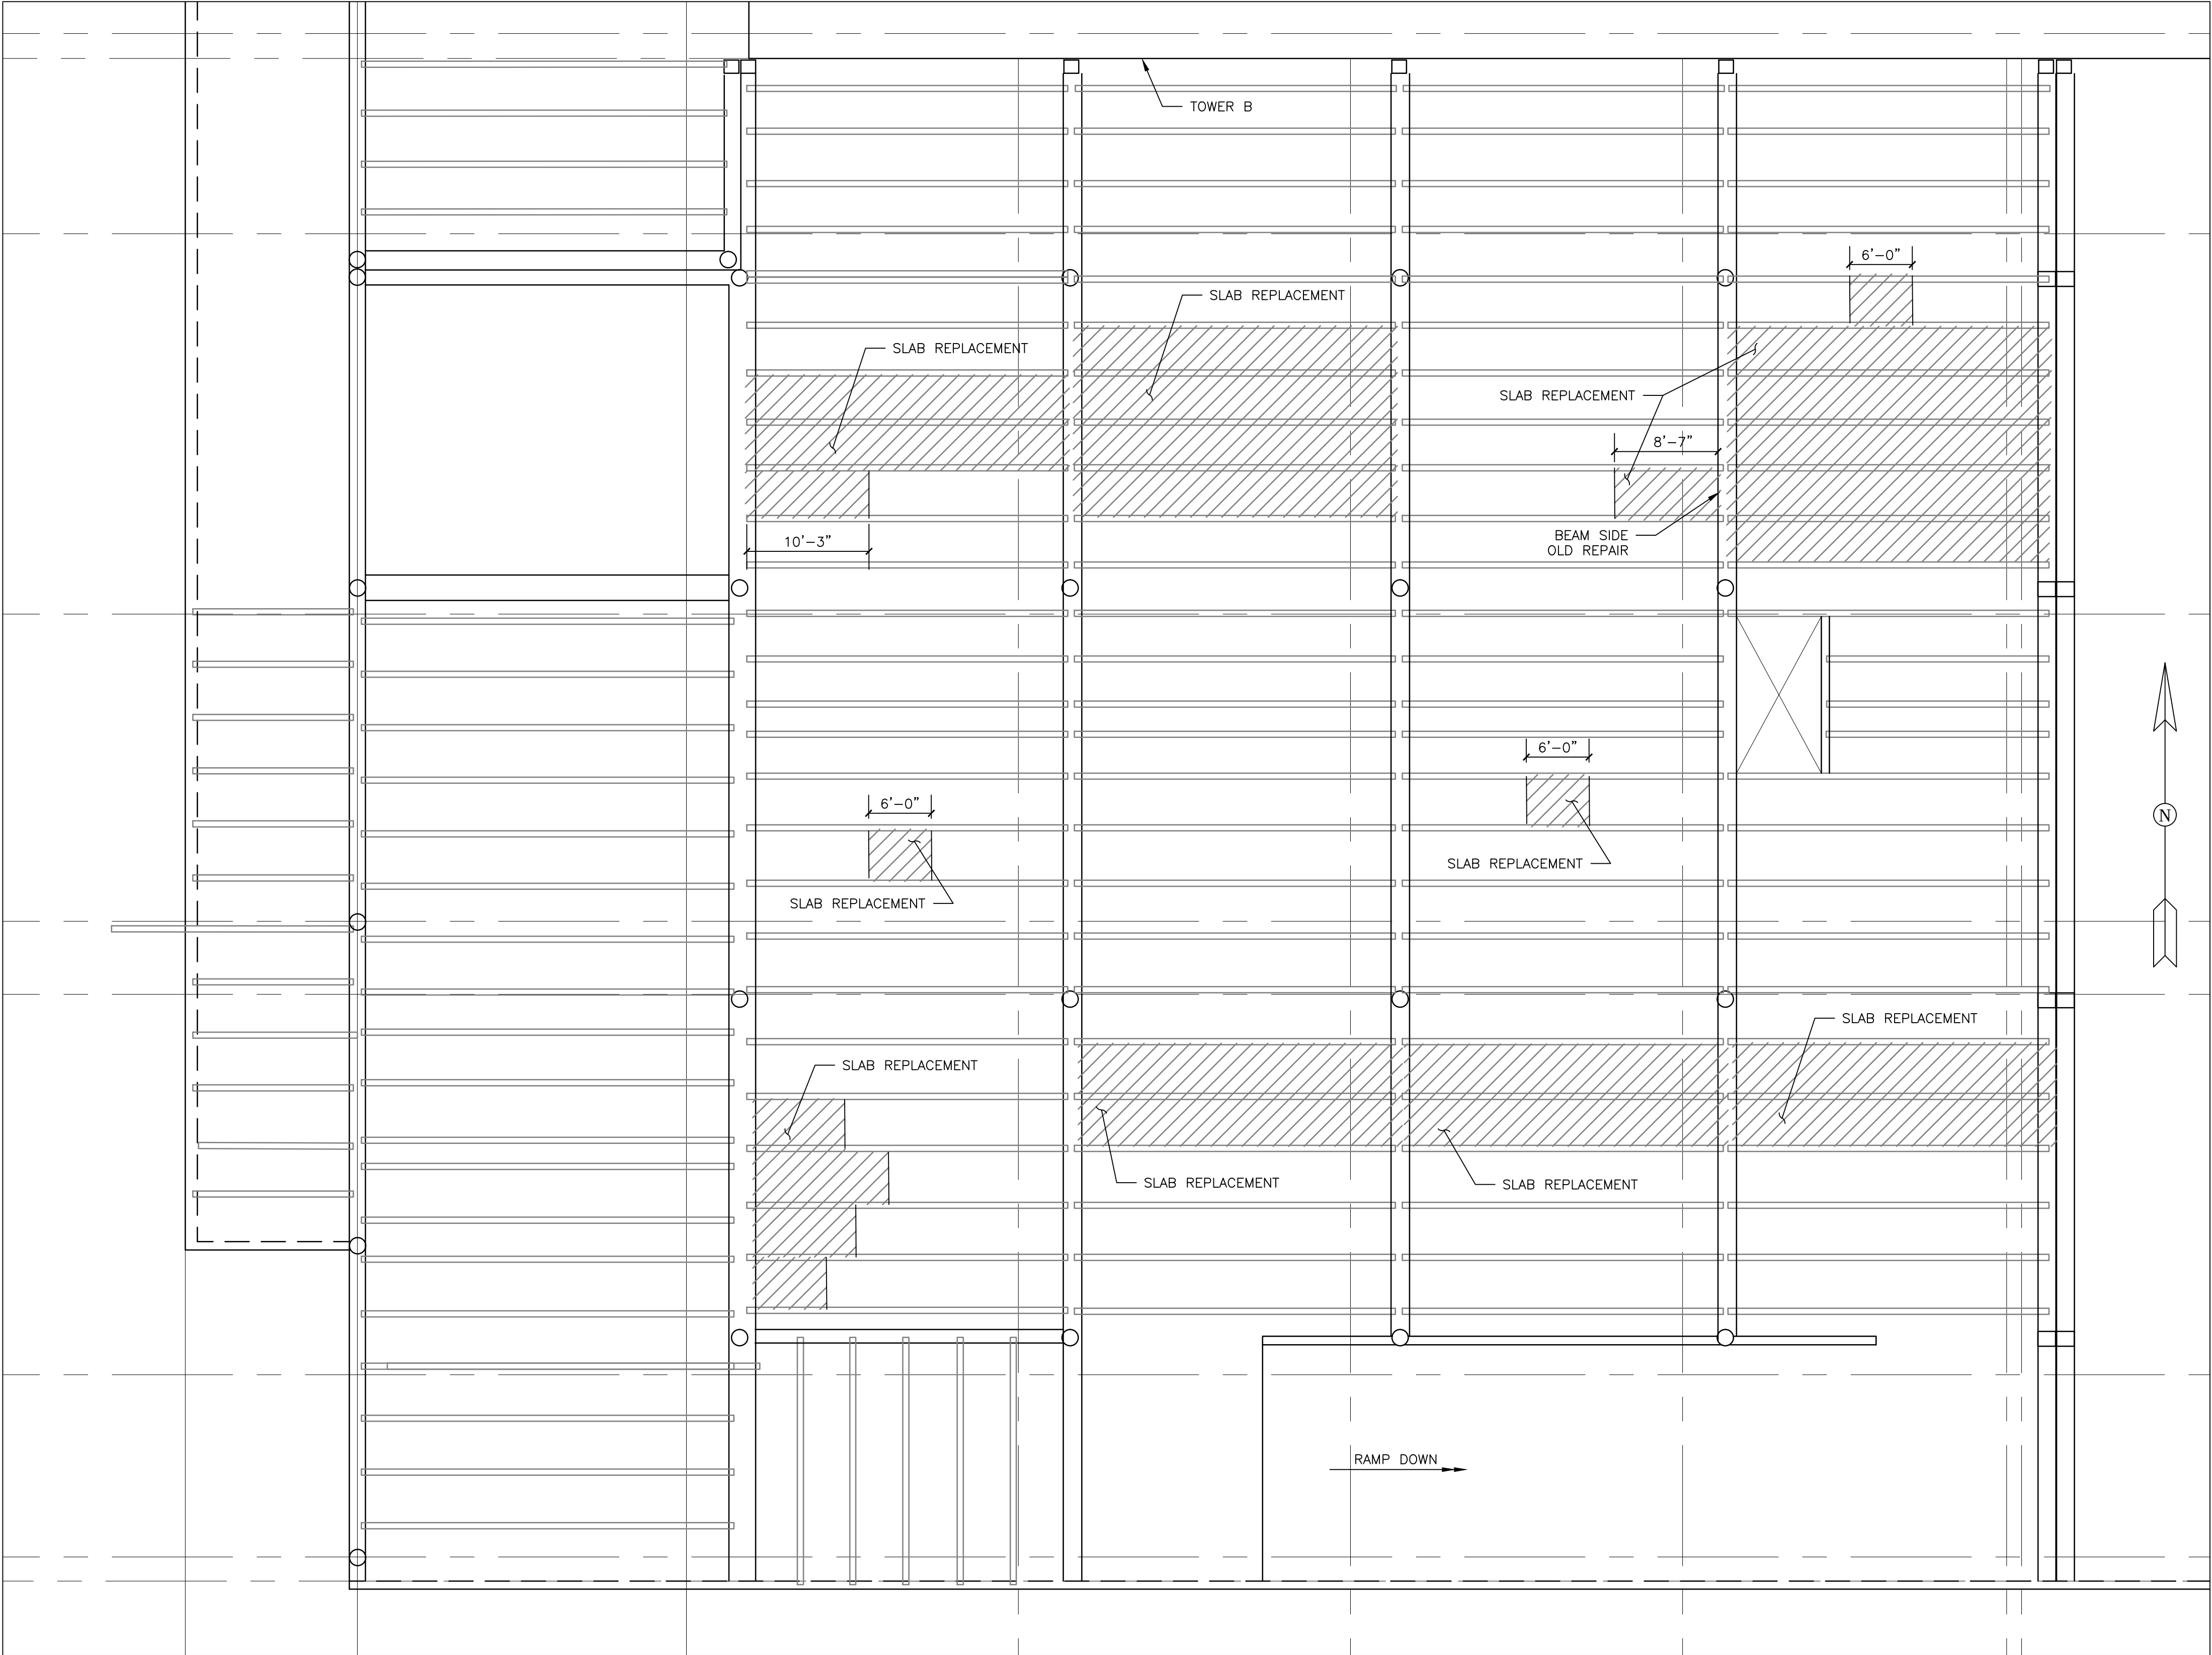

BRICKELL PLACE CONDOMINIUMS
1901 BRICKELL AVE.
MIAMI, FL 33129
GARAGE DECK REPAIRS

PROJECT No.:		REV	DESCRIPTION	DATE
DRAWN:	OL			
CHECK:				
APPROVED:				
DATE:				

HENRY S. KREH
FL. P.E. #39539

SD-6
